


# 78TH STREET IMPROVEMENTS • MERCY ROAD TO PACIFIC STREET

78th STREET PROJECT PHASING UPDATED 3-2021

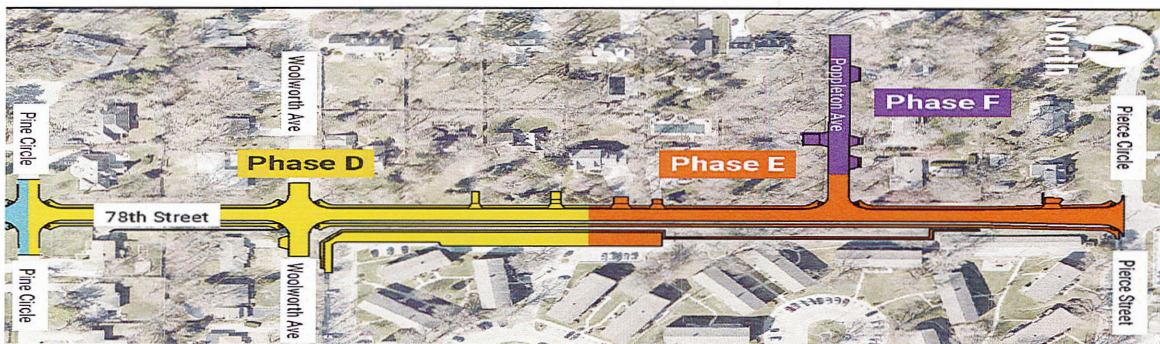

**Phase D** - The watermain installation is complete from Pine Circle to Woolworth Avenue. The remainder of work in Phase D from Pine Circle to Phase D/E phasing line as shown will resume in July with a Fall 2021 completion date. Resident driveways that are a part of Phase D will park on 78th Street, north of the Phasing line D/E when this work begins. You will also be notified as this work draws closer.

**Phase E** - Work is scheduled to begin the week of April 5 with an anticipated completion timeframe of late June. Resident driveways affected by Phase E south of Poppleton Avenue will park on 78th Street, south of the Phase D/E separation line. Residents north Poppleton Avenue will park along Pierce Circle.

**Phase F** - Poppleton Avenue west of 78th Street was completed in 2020. No further work anticipated except at the intersection of 78th & Poppleton Avenue only.

